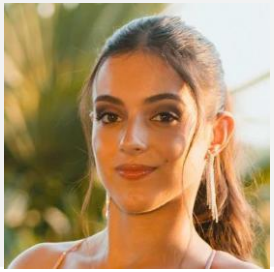
ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

LAPR3 2025/2026

Logistics on Rails - **SPRINT 1**

G092

Marília Lopes 1241243	Miguel Pereira 1241187	José Oliveira 1241277	Diogo Oliveira 1241883	Afonso Machado 1241182
				

Sprint planning – Sprint 1

Planned Start Date: 29/09/2025

Planned End Date: 26/10/2025

Real Start Date: 03/10/2025

Real End Date: 25/10/2025

SPRINT BACKLOG			
Number of stories	16		
Number of bugs	4		
Number of tasks	6		
Number of Management Tasks (Scrum)	4		
Number of team members		Planned: 4	Actual: 5
Total planned estimation vs execution		Planned hours: 32 Executed hours: 40	


Sprint 1 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USLP01	Yes				X	
USLP02	Yes				X	
USLP03	Yes				X	
USEI01	Yes				X	
USEI02	Yes				X	
USEI03	Yes				X	
USEI04	Yes				X	
USEI05	Yes				X	


Sprint 1 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USBD01	Yes				X	
USBD02	Yes				X	
USBD03	Yes				X	
USBD04	Yes				X	
USBD06	Yes				X	
USBD11	Yes				X	
USBD15	Yes				X	
USBD17	Yes				X	

Work assigned by team member

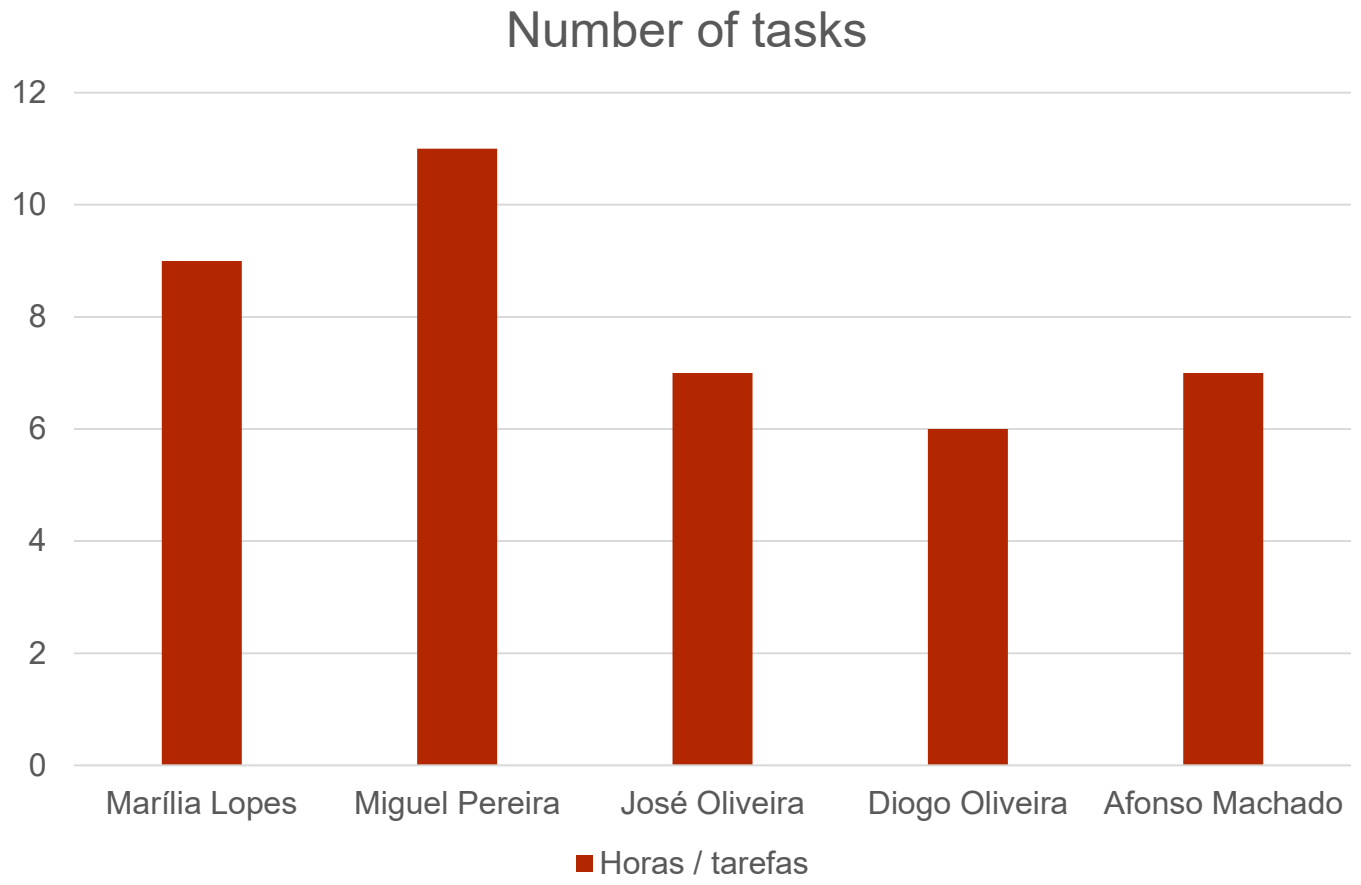

Work assigned by type (componente)

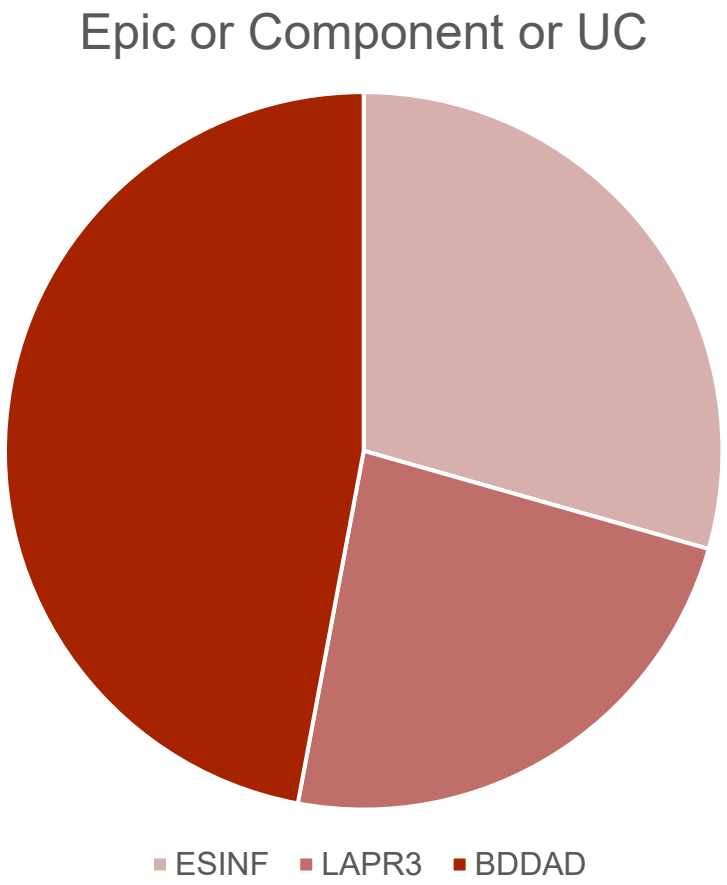

Issues / Assumptions / unanswered questions

Description	Responsible	Date / sprint	Related issue / item in Git
When the USEI02 was called by the US03 menu, the interface wasn´t getting the information for the allocations from the USEI02, but instead was always assuming non-existance of allocations.	Miguel Pereira	22/10/2025	**USPL02**
Questions about how to import data into USEI04, having to get .csv from USEI02 and USEI03.	Marília Lopes	23/10/2025	**USEI04**
Database errors on Oracle Live SQL, server downtime, and errors related to reserved words.	Diogo Oliveira and Marília Lopes	20/10/2025	**USDB03 and USBD04**

Daily Meetings

Date (of the meeting)	Place / duration	José Miguel Pereira	José Oliveira	Diogo Oliveira	Marília Lopes	Afonso Machado
02/10/2025	Class / 1 hour	x	x	x	x	x
06/10/2025	Online / 1 hour	x	x	x	x	x
08/10/2025	Class / 1 hour	x	x	x	x	x
11/10/2025	Online / 22 min	x	x	x	x	x
12/10/2025	Online / 30 min	x	x	x	x	x
18/10/2025	Online / 25 min	x	x	x	x	x
19/10/2025	Online / 15 min	x	x	x	x	x
21/10/2025	Online / 30 min	x	x	x		x
24/10/2025	ISEP / 25 min	x	x	x	x	x
25/10/2025	Online/ 5 min	x	x	x	x	

LLM performance assessment (Google Gemini)

Source file (File 1): Also used the project guide and a .zip file of our project repository.

Input (write down the prompt you used to ask for the performance assessment) :

Do a performance assessment on our team using the given files, make sure your response is split into an output file and another output (the first is a generalized assessment, and the second is a Team Member specific assessment). The Output file is in a readme and the output for the team members is 1 line only for each member.

LLM performance assessment - Output

Output file (File)

Output:

Marília Lopes: Led documentation (USLP01, Global Artifacts) and completed the complex USEI04 (Pick Path Sequencing) while managing data import and DB issues.
Miguel Pereira: Handled a high volume of cross-disciplinary tasks (USLP02, USBD15, UI design) and was central to the complex USEI01/USEI02 stories and bug-fixing.
José Oliveira: Delivered key BDDAD stories (USBD06, USBD11) and was a core contributor to the complex ESINF stories USEI01 and USEI02.
Diogo Oliveira: Built the database foundation by delivering the relational model (USBD02, USBD03) and tackled the USEI03 (Picking Plans) story while co-managing DB downtime.
Afonso Machado: Took ownership of the complex USEI05 (Returns & Quarantine) story and key BDDAD tasks USBD01 (Data dictionary) and USBD17.

Team Members' Opinion about the A.I. output:

ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

Sprint Retrospective

Date: 26/10

What went well?

- We completed all of our assigned tasks
- We maintained frequent communication
- Our board was always updated according to our work
- We had a constant work rhythm
- We managed to help each other
- Had frequent daily meetings

What went wrong?

- Encountered various bugs, that slowed down our progress

What we learned?

- Overcoming barriers in our progress, by searching alternatives
- Checking up on each others work and offer help to speed up work rhythm
- The reason behind the daily meetings, and how they are useful

Sprint Retrospective

Date: 26/10


Action items:

Overall Project performance:

- Comments: Our group is very satisfied with the results and performance during Sprint 1.

- LLM evaluation: 5

- How do you grade your performance (0-5): 5
- How do you grade your results (0-5): 5



ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

